New Custom Residence Schedule

Lasley Construction Company,LLC
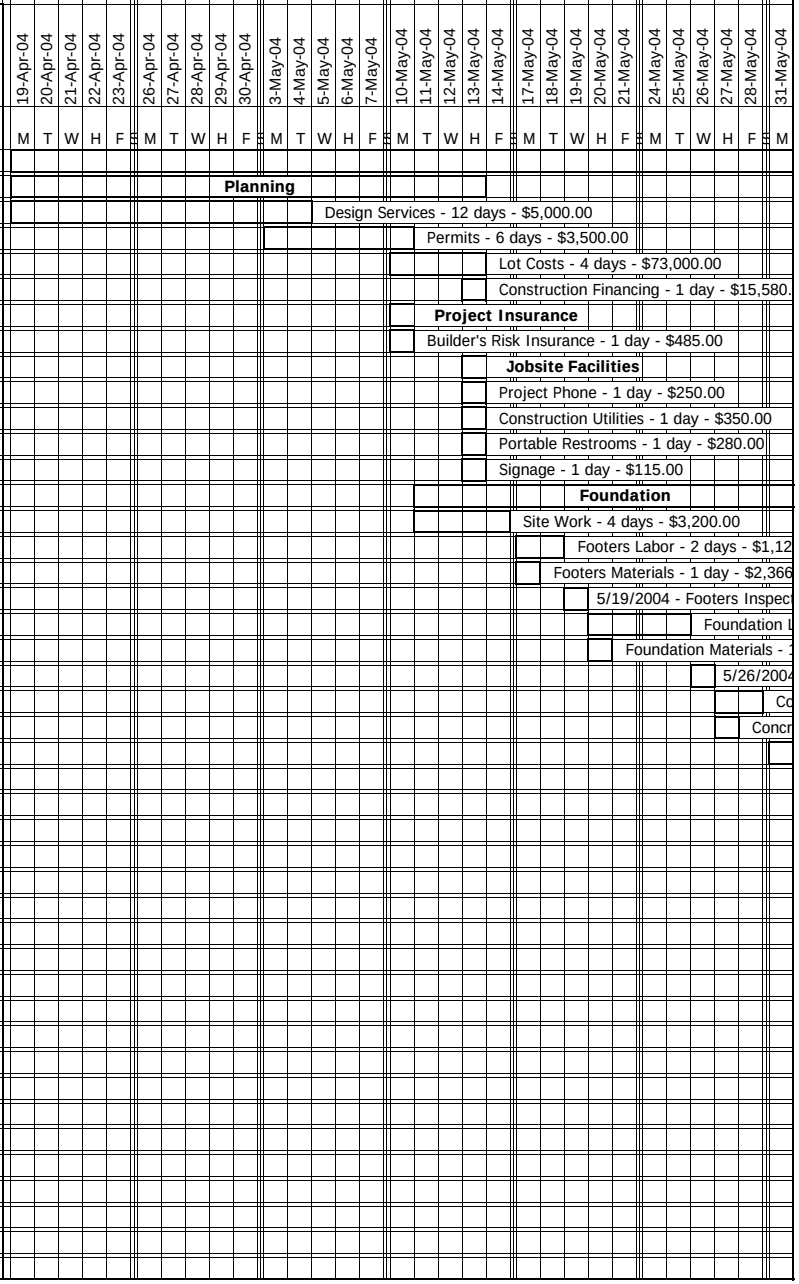
ID	Task	Start Date	End Date	Duration	Predecessor	% Complete
1	**Sandstone Residence**	**Mon Apr/19/04**	**Tue Sep/7/04**	**102 Days**		
2	**Planning**	**Mon Apr/19/04**	**Thu May/13/04**	**19 Days**		
3	Design Services	Mon Apr/19/04	Tue May/4/04	12		
4	Permits	Mon May/3/04	Mon May/10/04	6		0%
5	Lot Costs	Mon May/10/04	Thu May/13/04	4		
6	Construction Financing	Thu May/13/04	Thu May/13/04	1		0%
7	**Project Insurance**	**Mon May/10/04**	**Mon May/10/04**	**1 Day**		
8	Builder's Risk Insurance	Mon May/10/04	Mon May/10/04	1		
13	**Jobsite Facilities**	**Thu May/13/04**	**Thu May/13/04**	**1 Day**		
14	Project Phone	Thu May/13/04	Thu May/13/04	1		
15	Construction Utilities	Thu May/13/04	Thu May/13/04	1		
16	Portable Restrooms	Thu May/13/04	Thu May/13/04	1		
17	Signage	Thu May/13/04	Thu May/13/04	1		
19	**Foundation**	**Tue May/11/04**	**Mon May/31/04**	**15 Days**		
20	Site Work	Tue May/11/04	Fri May/14/04	4	8	0%
21	Footers Labor	Mon May/17/04	Tue May/18/04	2	20	0%
22	Footers Materials	Mon May/17/04	Mon May/17/04	1	20	
23	Footers Inspection	Wed May/19/04	Wed May/19/04	0	21	
24	Foundation Labor	Thu May/20/04	Tue May/25/04	4	23	
25	Foundation Materials	Thu May/20/04	Thu May/20/04	1	23	
26	Foundation Inspection	Wed May/26/04	Wed May/26/04	0	24	
27	Concrete Slab Labor	Thu May/27/04	Fri May/28/04	2	26	
28	Concrete Slab Materials	Thu May/27/04	Thu May/27/04	1	26	
29	Slab Inspection	Mon May/31/04	Mon May/31/04	0	27	
31	**Framing**	**Tue Jun/1/04**	**Fri Jun/18/04**	**14 Days**		
32	Framing Labor	Tue Jun/1/04	Wed Jun/16/04	12	29	0%
33	Floor System Materials	Tue Jun/1/04	Tue Jun/1/04	1	29	
34	Wall Framing Materials	Mon Jun/7/04	Mon Jun/7/04	1		
35	Ceiling Framing Materials	Thu Jun/10/04	Thu Jun/10/04	1		
36	Roof Framing Materials	Mon Jun/14/04	Mon Jun/14/04	1		
37	Roof Decking Materials	Mon Jun/14/04	Mon Jun/14/04	1		0%
38	Fascia & Soffit Materials	Fri Jun/18/04	Fri Jun/18/04	1		0%
40	Framing Inspection	Thu Jun/17/04	Thu Jun/17/04	0	32	
41	**Exterior Windows & Doors**	**Fri Jun/18/04**	**Fri Jun/18/04**	**1 Day**		
42	Windows	Fri Jun/18/04	Fri Jun/18/04	1	40	0%
43	Exterior Doors	Fri Jun/18/04	Fri Jun/18/04	1	40	
45	**Electrical Systems**	**Fri Jun/18/04**	**Mon Jun/28/04**	**7 Days**		
46	Electrical Labor	Fri Jun/18/04	Thu Jun/24/04	5	40	0%
47	Electrical Rough-In Inspection	Fri Jun/25/04	Fri Jun/25/04	0	46	
49	Underground Utilities	Fri Jun/25/04	Mon Jun/28/04	2	46	
50	**Plumbing**	**Fri Jun/18/04**	**Tue Jul/6/04**	**13 Days**		
51	Plumbing Labor	Fri Jun/18/04	Thu Jun/24/04	5	40	0%
52	Plumbing Rough-In Inspection	Fri Jun/25/04	Fri Jun/25/04	0	51	
53	Natural or Propane Gas	Fri Jun/25/04	Mon Jun/28/04	2	51
